Key

Lorg Construction Programme

ID	Task Name	Duration
1	Total Programme	24 mons
2	Winter Shutdown	4 mons
3	Mobilisation	5 days
4	Compound / Borrow Pit Set-up	4 wks
5	Access tracks	165 days
6	Turbine pads and foundations	150 days
7	Control Building	120 days
8	Electrical Installation	75 days
9	Electrical commissioning	30 days
10	Turbine erection	5 mons
11	Turbine commissioning and testing	6.5 mons
12	Reinstatement	150 days

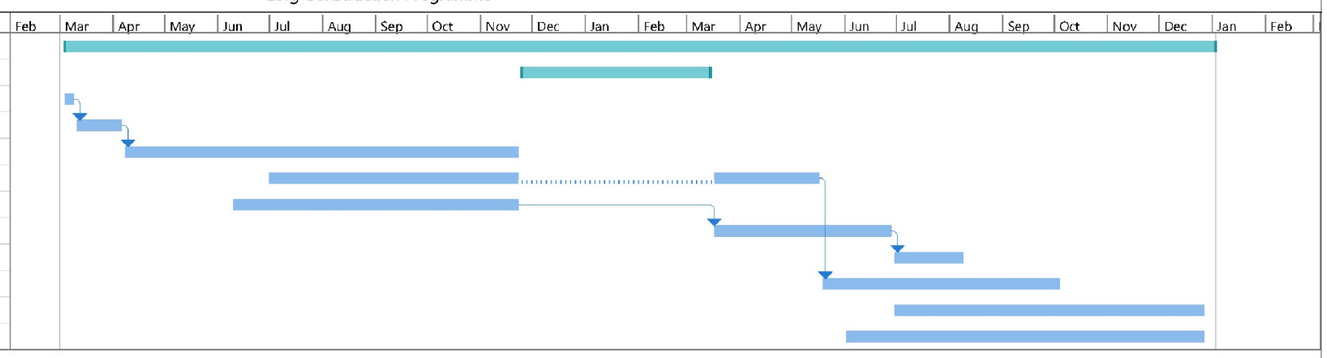

Lorg Wind Farm
Environmental Impact Assessment Report

Figure 3.10 Construction Programme

November 2022

C:\Users\steven.fitzpatrick\Desktop\Lorg\ArcGIS\MXD\Lorg 24 month construction programme v2.1.mxd Originator: steven.fitzpatrick
